

Shady Oak Road

Project Update

Project website: edenprairie.org/shadyoak

May 6, 2013

SHADY OAK ROAD CONSTRUCTION PROGRESS UPDATE

May 6, 2013 – May 8, 2013

1. Roadway Construction:

- a. Finished installation of temporary signal systems to be used during construction.
- b. Constructed new watermain, storm sewer, and sanitary sewer.
- c. Began construction of the South Pond.
- d. Installed temporary pavement and concrete barrier in preparation for Stage 1 construction of north bound Shady Oak Road.



Concrete barrier & temporary pavement installed for Stage 1 traffic control.

2. Future Construction:

- a. Begin construction of new north bound Shady Oak Road.
- b. Begin construction Retaining Wall B under Highway 62 overpass.

3. Traffic Control/Detours

- a. Existing lane closures on Shady Oak Road are anticipated to end next week, at which time all traffic will be moved to the west side of Shady Oak Road.
- b. Temporary traffic signals will be activated at 9 a.m. on Monday, May 6, expect delays.

Hotline:
952-279-8000

Email:
info@shadyoakroad.com





Shady Oak Road


Project Update

Project website: www.edenprairie.org/shadyoak

May 6, 2013

Hotline:
952-279-8000

Email:
info@shadyoakroad.com

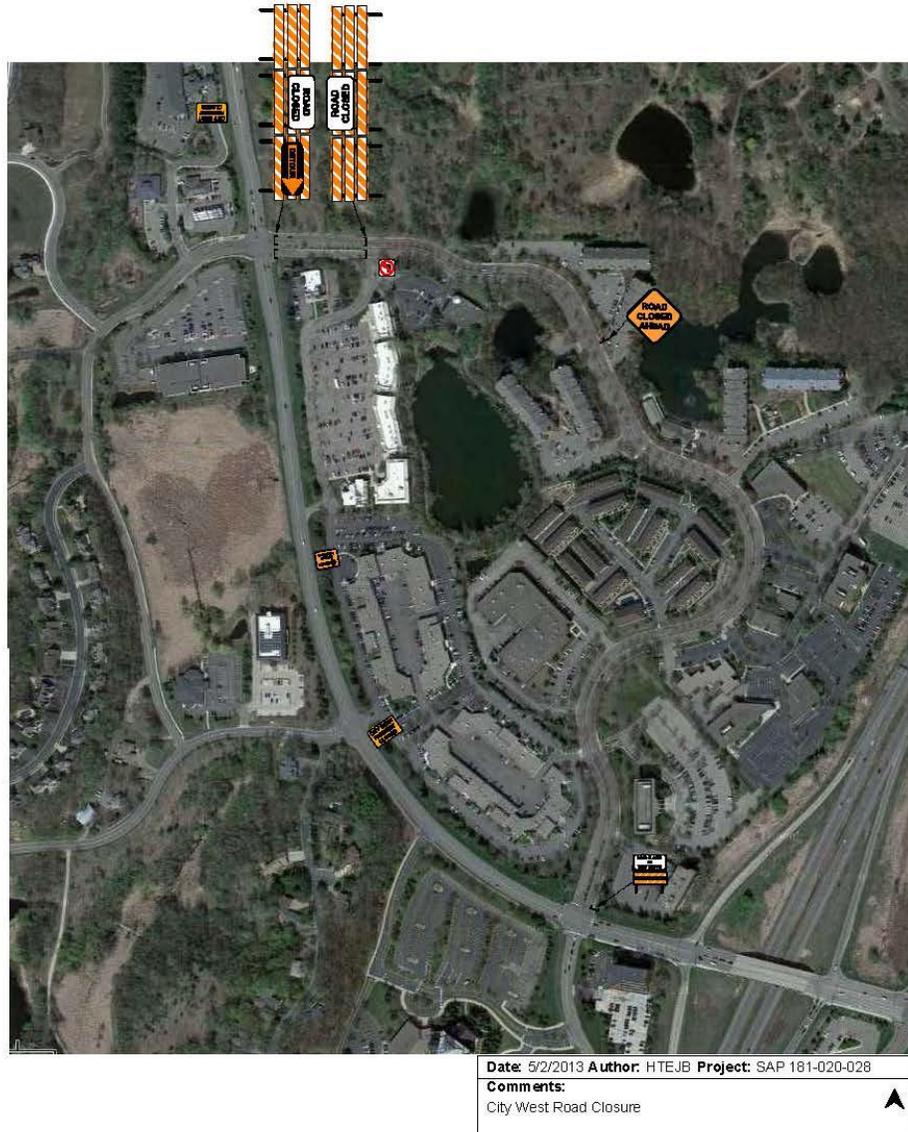

- c. The contractor plans to install sanitary sewer, water main and storm sewer in the City West Parkway leg of the Shady Oak Road intersection on Tuesday and Wednesday of this week (5/7 and 5/8). This work will be completed under a full closure of City West Parkway between Shady Oak Road and the Shady Oak Center access.

This work is weather dependent and subject to change.

